CITY OF ANN ARBOR COMMERCIAL RECYCLING PROGRAM IMPLEMENTATION TIMELINE
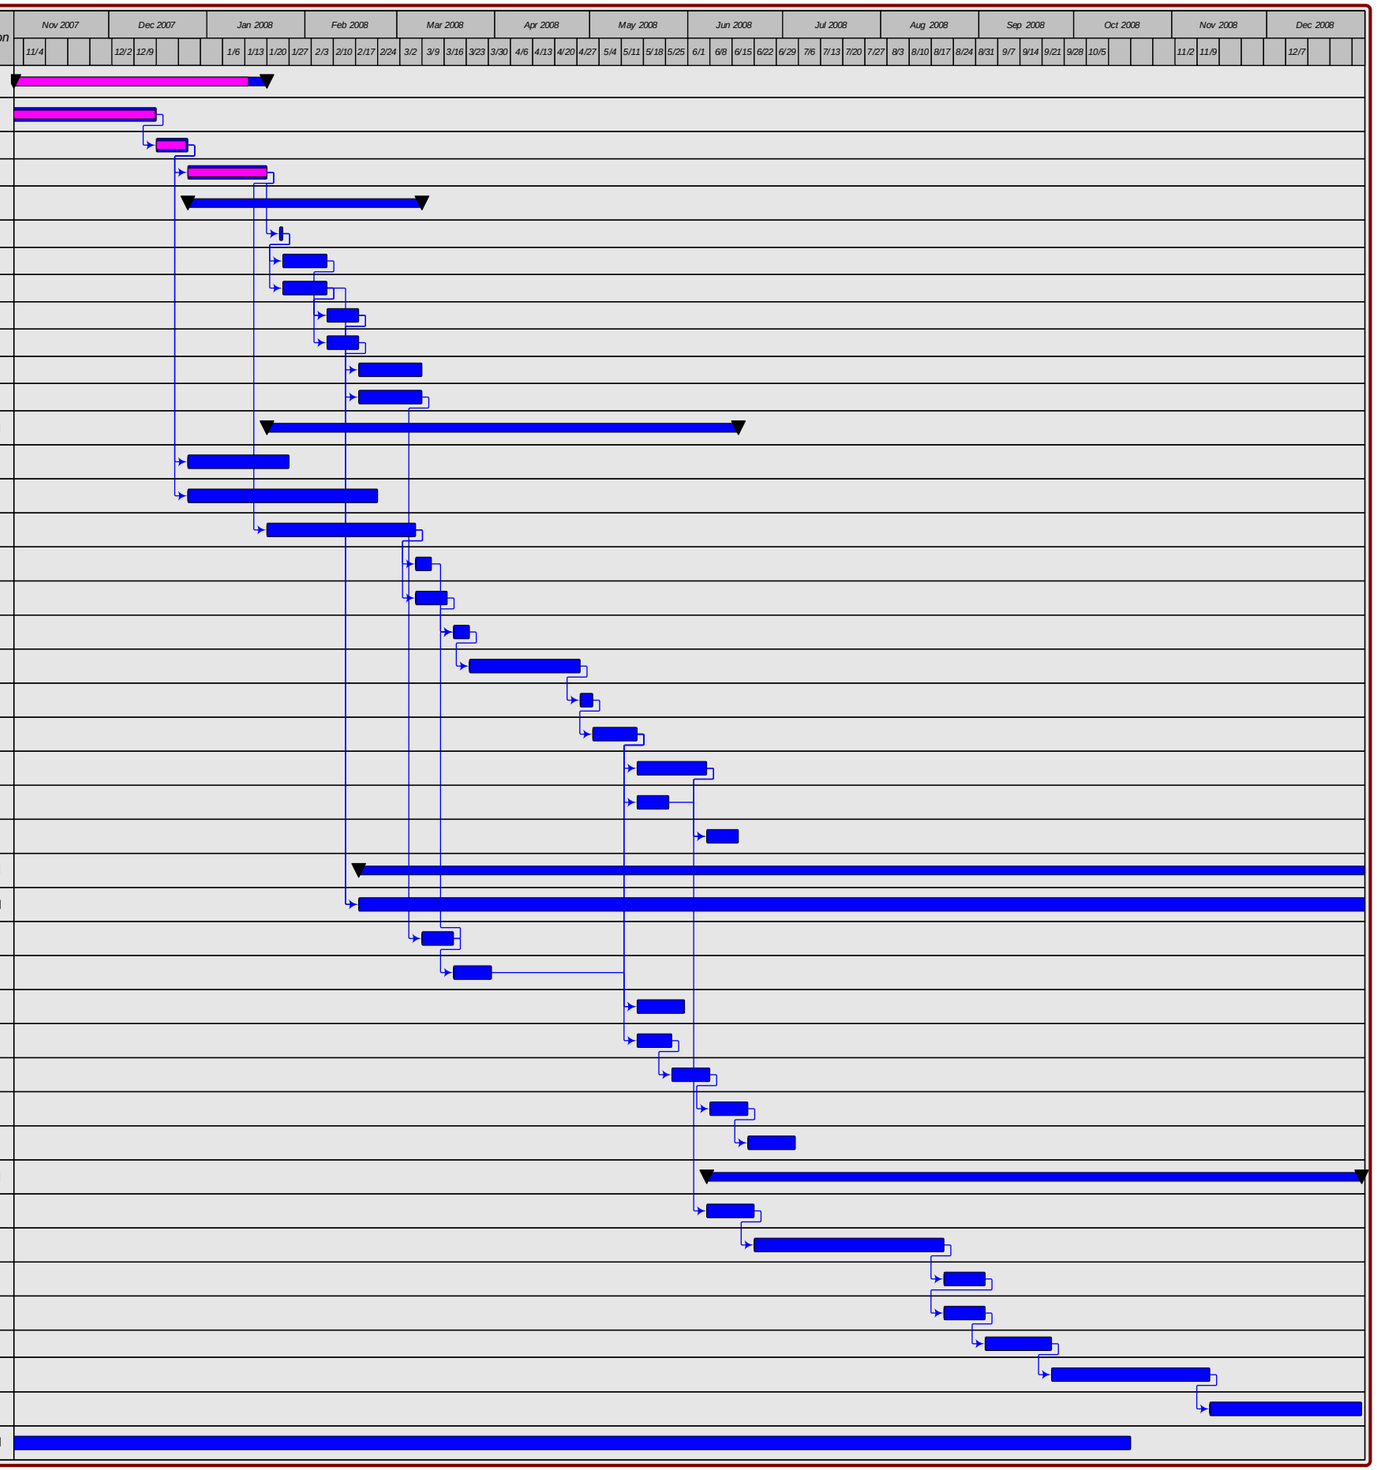
ID	Task Name	Start	End	Duration
1	**Develop Preliminary Content for Next Phase of Documents**	**11/1/2007**	**1/19/2008**	**80d**
2	Draft First Cut Documents(Ordinances/Specs/etc.)	11/1/2007	12/15/2007	45d
3	Work Group Edit of Documents	12/16/2007	12/25/2007	10d
4	Revised Drafts for Distribution including "Review Instructions"	12/26/2007	1/19/2008	25d
5	**Re-Engage Key Stakeholders and Implementation Parties**	**12/26/2007**	**3/8/2008**	**74d**
6	Meeting #1 – Kick-off	1/24/2008	1/24/2008	1d
7	Document Review Period (w/Instructions)	1/25/2008	2/7/2008	14d
8	Sue McCormick/DPS Step 1 Distribution/Review Opportunity	1/25/2008	2/7/2008	14d
9	Meeting #2 – Document Comments Due/Issues Brainstorm	2/8/2008	2/17/2008	10d
10	Communications Campaign Collaborators Convened	2/8/2008	2/17/2008	10d
11	Meeting #3 – Issues Discussion/Process Input	2/18/2008	3/8/2008	20d
12	First "Friends Recruiting Friends" Meeting Ownership Building	2/18/2008	3/8/2008	20d
13	**Market Based Informing of Planning/Decision Making**	**1/20/2008**	**6/16/2008**	**149d**
14	Further Refine Schedules/Background Data Work	12/26/2007	1/26/2008	32d
15	Negotiations with Existing Operating Partners	12/26/2007	2/23/2008	60d
16	RFEI Process to Solicit Input from Vendors	1/20/2008	3/6/2008	47d
17	Sue McCormick/DPS Step 2 Distribution/Review	3/7/2008	3/11/2008	5d
18	Refining Request for Proposals Documents	3/7/2008	3/16/2008	10d
19	Request for Proposals Release	3/19/2008	3/23/2008	5d
20	Proposal Preparation by Vendors	3/24/2008	4/27/2008	35d
21	Proposal Due Date	4/28/2008	5/1/2008	4d
22	Proposal Evaluation/Interviews/Clarifying Questions	5/2/2008	5/15/2008	14d
23	Proposal Packaging for Recommendations	5/16/2008	6/6/2008	22d
24	Sue McCormick/DPS Step 3 Distribution/Review	5/16/2008	5/25/2008	10d
25	Draft Recommendations/Supporting Docs (e.g. Ordinances)	6/7/2008	6/16/2008	10d
26	**Involve Key Stakeholders/Implementation Parties in Preparing**	**2/18/2008**	**1/21/2009**	**339d**
27	Communications Campaign	2/18/2008	1/21/2009	339d
28	Merchant Association Info Sessions	3/9/2008	3/18/2008	10d
29	Meeting #4 Primer Meeting (RFEI Results/Program Summary)	3/19/2008	3/30/2008	12d
30	Meeting #5 to Consider RFP Results/Program	5/16/2008	5/30/2008	15d
31	Merchant Association Results/Input Sessions	5/16/2008	5/26/2008	11d
32	Meeting #6 to Consider Recommendations	5/27/2008	6/7/2008	12d
33	First "Friends Recruiting Friends" Presentations	6/8/2008	6/19/2008	12d
34	Meeting #7 (Final in Budget) for Recommendations/Campaign	6/20/2008	7/4/2008	15d
35	**Preparing Recommended Action Items**	6/7/2008	**12/30/2008**	**207d**
36	Work Group Compiles Recommendation Documents	6/7/2008	6/21/2008	15d
37	Work Group Finalizes Action Item Package	6/22/2008	8/20/2008	60d
38	Sue McCormick/DPS Step 4 Review/Action	8/21/2008	9/2/2008	13d
39	Roger Fraser/Administration Review/Action	8/21/2008	9/2/2008	13d
40	Environmental Commission Review/Action	9/3/2008	9/23/2008	21d
41	City Council Review/Action	9/24/2008	11/12/2008	50d
42	2nd Year Budget Amendment or 2009/10 Budget Year	11/13/2008	12/30/2008	48d
43	Implementation Demand/Response	11/1/2007	10/18/2008	353d
